

ATTACHMENT A


JUSTIS

Schedule Overview & Review

April 23rd 2009

Mayor's Office of Criminal Justice
City & County of San Francisco

JUSTIS Components

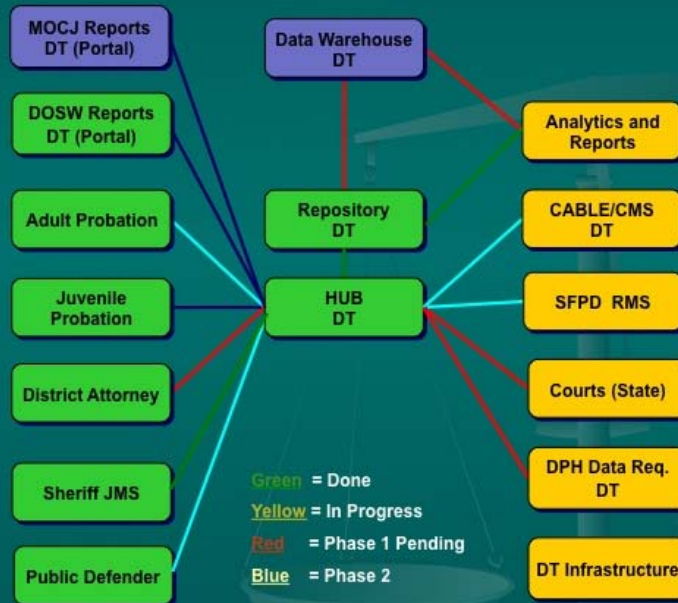

JUSTIS Program – April 2009 Plan Construction Process

- Multiple Project Plan Consolidation & Review - One United Plan
- Working sessions with DT Operations & Infrastructure addressing Sheriff Go-Live dates & constraints
- Communication with Departments to review your remaining components
- Council Presentation
- Reset Tasks / Plan Modifications per Council Review
- Finalize Remaining Dates & Commitments with O&I
- Final Schedule Submitted to Mayor's Office

Mayor's Office of Criminal Justice
City & County of San Francisco



JUSTIS Program – Milestones to Production

Sheriff: Jail Management System (JMS)

- JMS Tested & Currently Ready for Deployment
- Time in Custody Report needs to be operational
- CITRIX Completion & Support May 14/09
- Shared JMS / RMS Server Environment May 21/09
- JMS / Hub / CMS Testing Estimated Completion May 22/09
- Production System Handoff to DT & Go Live Ready June 04/09
- Community Justice Center (CJC) Connection work under way

Mayor's Office of Criminal Justice
City & County of San Francisco



JUSTIS Program – Milestones to Production

Public Defender: GIDEON Case Management System

- GIDEON – Estimated Completion by end of July 2009
- No outstanding Infrastructure tasks
- Hub Interface: Vendor side is complete, DT side of interface partially complete. Further development and testing required pending resource availability.
- Estimated Schedule: End to end testing should be complete and GIDEON production ready by October 2009.



JUSTIS Program – Milestones to Production

Adult Probation: cTag Case Management System

- cTag – Complete & Internally Deployed
- No outstanding Infrastructure tasks
- Hub Interface: Statement of Work still in negotiations with Syscon. Target date for interface completion is 8 to 11 months after SOW is completed.
- Supervised Release File (SRF) is 80% complete. One month to complete when staff assigned.
- CJC Connectivity work is under way



JUSTIS Program – Milestones to Production

District Attorney: DAMION Case Management System

- DAMION – Complete & Internally Deployed
- No outstanding infrastructure tasks
- Hub Interface: Vendor review of DT interface specification complete. Awaiting DT review of DA use cases and transaction specification.
- CJC Connectivity is under way

Department on the Status of Women

- DV & Information Portal – Design & Prototype is complete
- Request for data has been reviewed by the Police Department
- JUSTIS staff have started further analysis to determine if the Hub can provide DOSW data prior to Police go-live.

Mayor's Office of Criminal Justice
City & County of San Francisco



JUSTIS Program – Milestones to Production

Police Department: Records Management System (RMS)

- Project Status & Schedule Estimates under review by Police Department

Superior Courts (State): CX2000

- CX2000 – Still in active development
- Need support from DT JUSTIS for conversion data
- No estimated dates currently available from Courts on system availability.

Mayor's Office of Criminal Justice
City & County of San Francisco



JUSTIS Program – Staffing

Immediate:

- Utilize Vendors / Consultants when resources unavailable
- Contract for CITRIX Support starting this coming Monday
- Reengage PlanGraphics – Spoke augmentation & documentation
- Reengage Oracle Consultant – Complete DT staff training & Public Defender Interface
- Renew contract for Owens Information Systems
- Reengage ITPM
- Fill two outstanding JUSTIS Positions
- Fill networking position
- Stagger training for DT Staff to Oracle University
- Cross training between DT Staff on spokes & Hub functions

